

PROJECT UPDATE

Issue No. 2
May 2015

LR Elem/EJMS Middle School Maintenance



Located existing utilities and formed slab for new chillers.



Demolished openings for O. H Coiling doors on the North side.



Removed existing equipment.



Installed plumbing for new fixtures.

Progress in the last 30 days:


1. EJMS Middle School:

- A. Located existing utilities.
- B. Formed and installed the Chiller pad.
- C. Began masonry work.
- D. Demolished openings for o. h. coiling doors at the north side of the building.

- E. Continued working on plumbing and finishes.
- F. Received boilers, roof curbs and VAC boxes.
- G. Continued shop submittals.

2. Laura Reeves Elementary:

- A. Continued shop submittals.

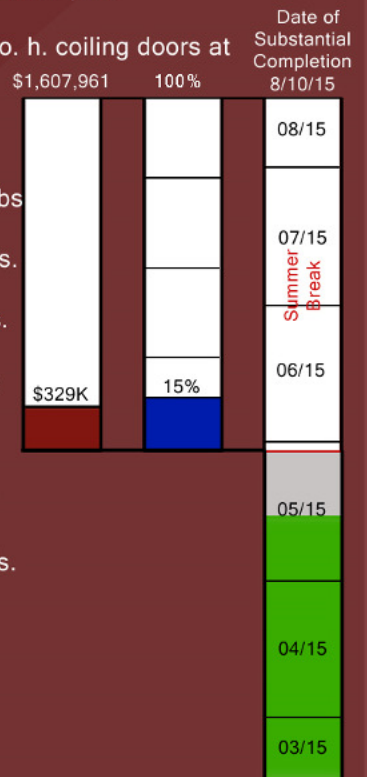

Scheduled for the Next 30 days:

1. EJMS Middle School:

- A. Install OH Coiling doors.
- B. Mount chillers on pads.
- C. Finish restroom plumbing work and finishes.
- D. Continued shop submittals.

2. Laura Reeves Elementary:

- A. Continue shop submittals.

■ GMP Money Authorized to Date
■ Completion of Project
■ Schedule for Project



Silsbee I.S.D.

